




#SRCTRANSFORMS

Updates on Current Transformations & Maintenance Works

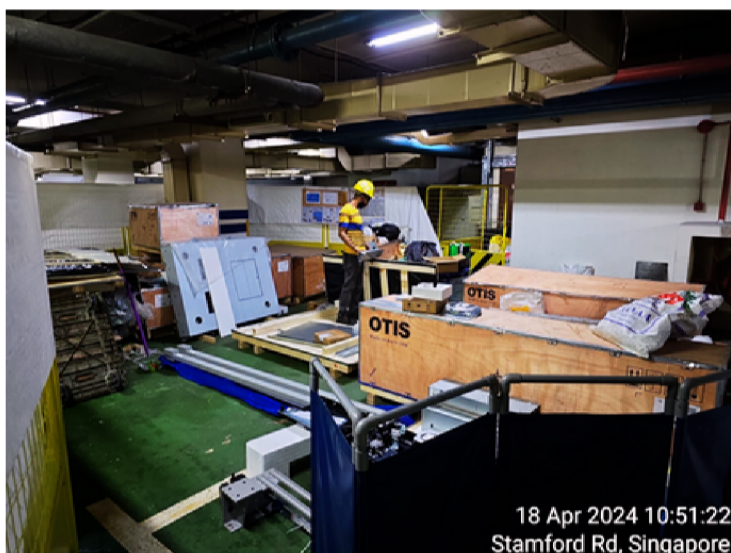

Lift Upgrading Project Updates

Due to the unexpected breakdown of the old service lift and a delay in lift pit strengthening work, the project schedule has been slightly extended.

Presently, work on the backend service lift is underway to be completed by end May 2024.



Subsequently, passenger lift no. 2 will undergo upgrading works and is scheduled to conclude by end August 2024.

Finally, passenger lift no. 1 is anticipated to be completed by end November 2024.

Chilled Water Retrofit Project Updates

After multiple rounds of energy audits, gap analysis, and submissions to the relevant authorities, the service provider is ready to import the chillers from overseas.

Expected delivery is in July 2024, on schedule for completion by the end of August 2024.



This image is for illustrative purposes only and does not represent the actual chiller unit.



The Courtyard Project Updates

Our beloved Courtyard, cherished by our members, is nearing completion, with the final stage of works scheduled to finish by end April 2024.

Anticipate the refurbishment and reorientation of 2 tennis courts, 2 multipurpose courts, and a revamped multipurpose pitch, promising a more dynamic and vibrant space for our community to enjoy.

Maximizing the usage of our space during the prolonged 7 months of public events at the Padang.

[HTTPS://SRC.ORG.SG/](https://src.org.sg/)
